

Project Planning Phase

Project Planning (Product Backlog & Sprint Planning)

Date	31 July 2026
Project Name	Indoor Gardening Services Management (IGSM)
Platform	ServiceNow

Done by Dega Leela Ramana

Sprint	Epic	Story ID	User story / task	Story Points	Priority
Sprint-1	Application Setup	US-1	Create IGSM scoped application and define application roles.	3	High
Sprint-1	Data Model	US-2	Create X_igsm_indoor_garden_request table and required fields.	5	High
Sprint-1	User & Group Setup	US-3	Create IGSM Technicians and IGSM Managers groups.	2	High
Sprint-2	Service Catalog	US-4	Create record producer and map variables to the request table.	5	High
Sprint-2	Workflow Automation	US-5	Implement approval workflow, technician assignment, and notifications.	8	High
Sprint-3	SLA Configuration	US-6	Configure Response SLA and Completion SLA for requests.	3	High
Sprint-3	Security (ACLs)	US-7	Implement role-based and requester-based ACLs.	5	High
Sprint-4	Business Rules	US-8	Add backend validations and prevent invalid state changes.	5	Medium
Sprint-4	Client Scripts	US-9	Implement UI validations and record producer client scripts.	3	Medium
Sprint-4	Testing & Validation	US-10	Validate end-to-end workflow, roles, SLAs, and access controls.	5	High

Sprint Tracker & Velocity Calculation

Sprint tracker

Sprint	Total Story Points	Duration	Sprint Start	Sprint End	Completed	Release Status
Sprint-1	10	5 Days	01 Aug 2026	05 Aug 2026	10	Completed
Sprint-2	13	5 Days	06 Aug 2026	10 Aug 2026	13	Completed
Sprint-3	8	5 Days	11 Aug 2026	15 Aug 2026	8	Completed
Sprint-4	13	5 Days	16 Aug 2026	20 Aug 2026	13	Completed

Velocity calculation

Total estimated story points: 44


Number of sprints: 4

Average velocity: 11 story points per sprint

Velocity = Total Story Points Completed / Number of Sprints = 44 / 4 = 11 story points per sprint.

Burndown Chart

Sprint-4 Burndown (13 Story Points)

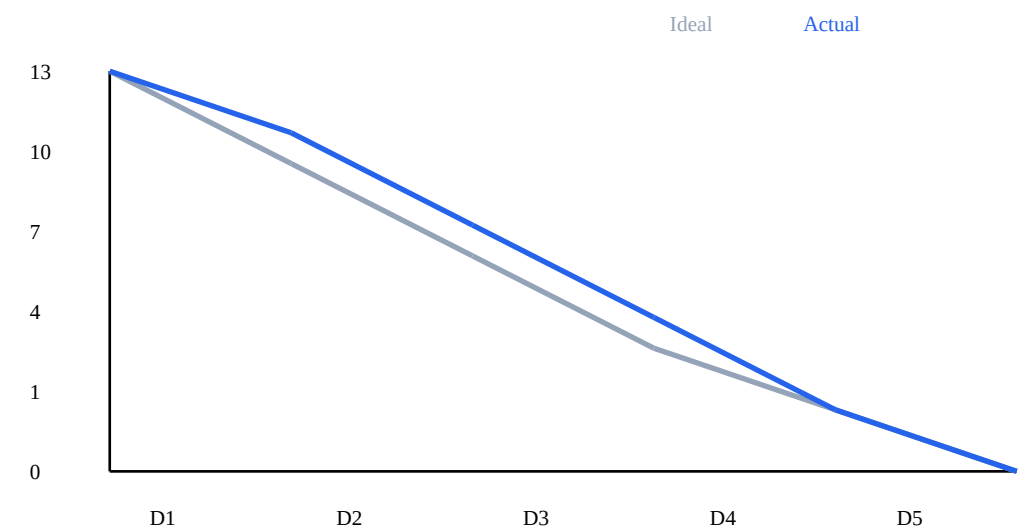

The burndown chart shows the remaining story points across the five-day sprint. The actual burndown closely follows the ideal trend and reaches zero remaining story points by the end of Sprint-4.
